


## Finalization of Planning Study 2018-2019



## Capital Planning and Procurement Processes 2019-2020

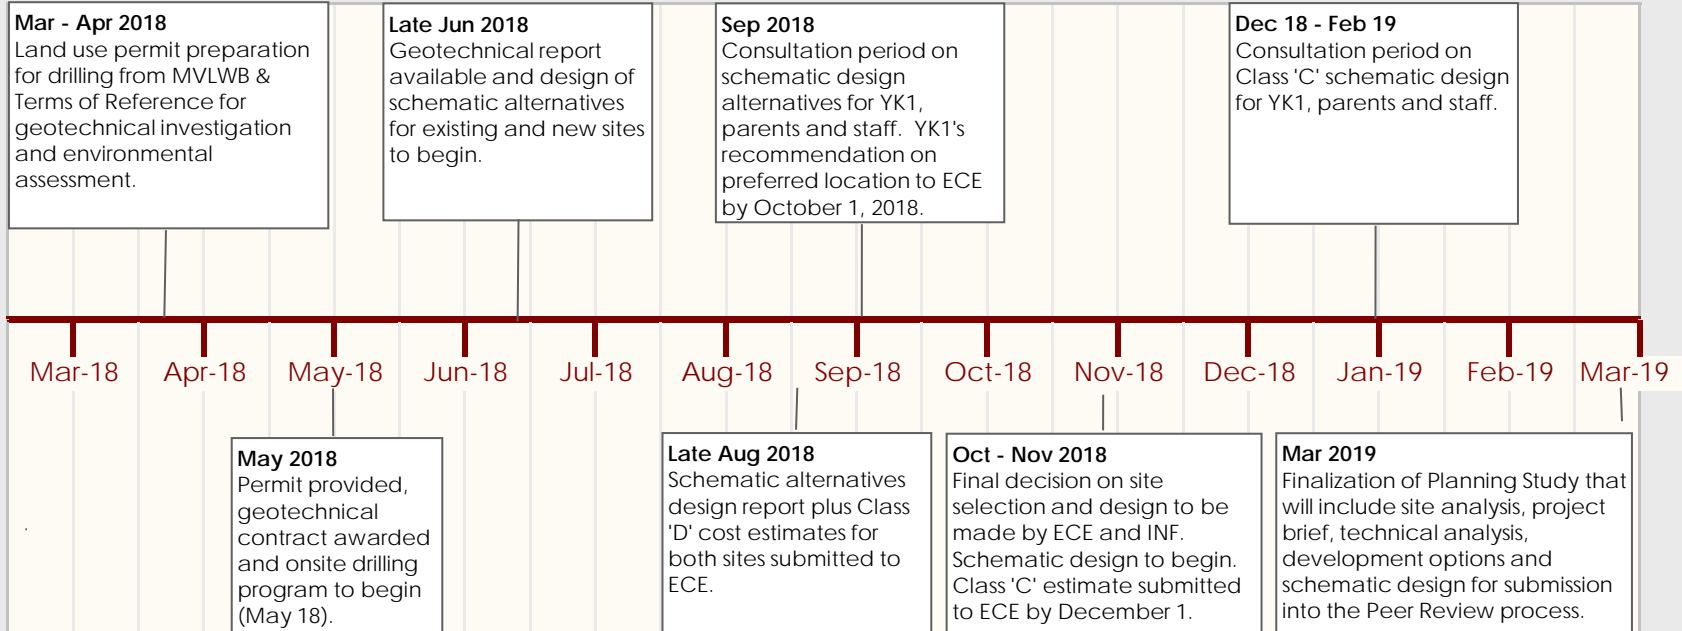

Note: The procurement process timeline assumes the J.H. Sissons project is included in the 2020-2021 Capital Plan and that plan is approved by the Legislative Assembly in October 2019.

# Procurement Processes 2020-2021

## Apr - Jul 2020

Detailed design development and technical review. This is the phase following schematic design during which preliminary drawings and outline specifications are developed.


## Jan - Mar 2021

Tender of project and award.

## Aug 2020 - Jan 2021

Preparation of construction documents. These are the final architectural, structural, mechanical, electrical and civil design documents prepared or assembled by architects and engineers for communicating the project design for construction and administering the construction contract.

Apr-20   May-20   Jun-20   Jul-20   Aug-20   Sep-20   Oct-20   Nov-20   Dec-20   Jan-21   Feb-21   Mar-21

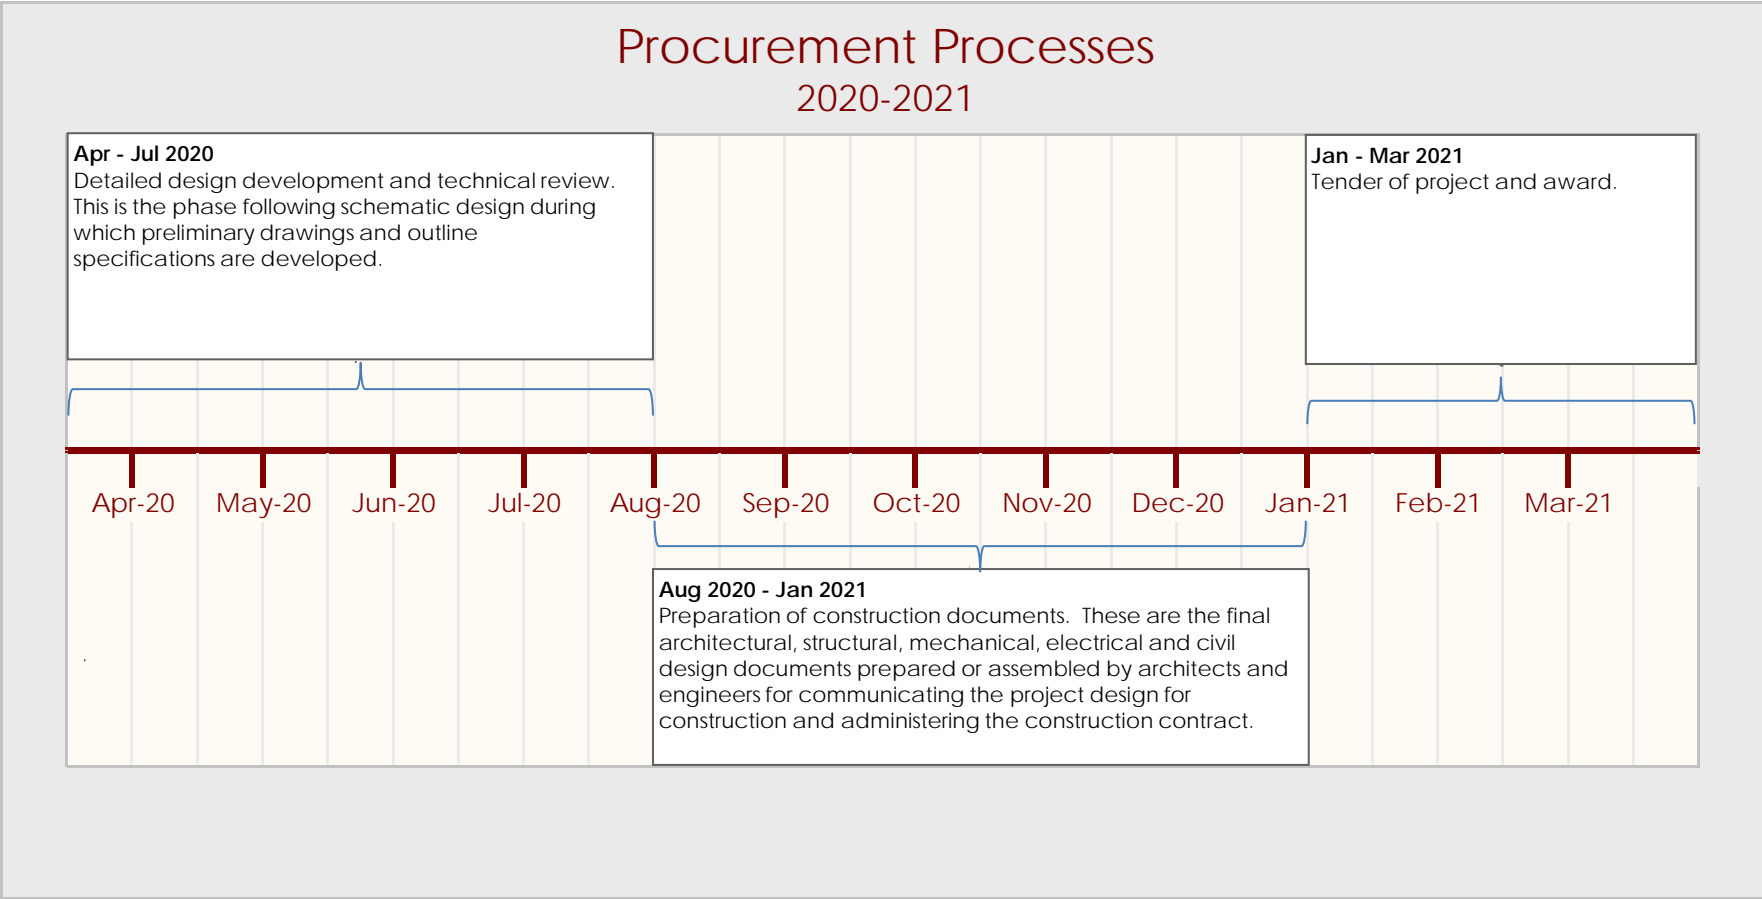

# Construction 2021-2024

Existing Site

**Jul - Oct 2021**  
Demolition and HAZMAT  
remediation of existing school.

**Nov 2021 - Aug 2023**  
Year 1 and Year 2 of construction.

Apr-21

Jun-21

Sep-21

Jan-22

Apr-22

Jun-22

Sep-22

Jan-23

Apr-23

Jun-23

Sep-23

Jan-23

Summer  
2024

**July 2021 - August 2023**  
Year 1 and Year 2 of construction.

**Aug 2023 - Oct  
2023**  
Demolition  
and HAZMAT  
remediation of  
existing school

**Summer 2024**  
Landscaping  
of old school  
site

New Site
